LSC
LOGISTICS & SUPPLY CHAIN CLUB

LOGICHAIN 2026
Round 2A: LABYRINTH


TEAM: SUPERNOVA



BÙI MINH PHƯƠNG



TRẦN THU HÀ

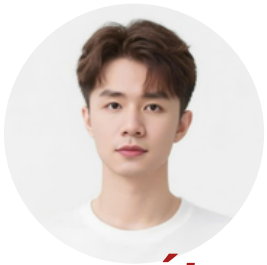

PHẠM ĐỨC TRÍ



TÂN HỒNG PHONG

Executive summary

From potential orders to profitable, compliant growth

LSC
LOGISTICS & SUPPLY CHAIN CLUB

SITUATION

TEXIN, a Vietnamese sportswear maker, sold **5.02M pcs** (**USD 19.28M** EXW) to EU buyer **LSC** in 2026. All dyeing and finishing steam comes from a **coal boiler**.

Coal boiler
300,000 GJ

→ **28,380 t**
CO2e baseline
2026 (index 100)

→ **LSC potential orders**
if ESG roadmap accepted:
+22% +25% +28%
(2027, 2028, 2029)

COMPLICATION

Caps tighten every year
-15% in 2027 to **-64%** by 2031 (Emission Target)

Growth raises emissions
On coal, 2027 = **31,786t** vs cap **24,123 t**

CAPEX is indivisible
Firing core = **88.3%** of USD **940,500**

Profit floors each year
NPM ≥ -10%, ≥ -8%, then > 0%

QUESTION

How should TEXIN **phase the USD 940,500 ESG CAPEX** to convert LSC's potential orders into **profitable growth**, while meeting **every buyer cap** and **every P&L floor** from 2027 to 2031?

ANSWER

01 **Front-load:** Tranche 1 **USD 896,500 (95.3%)** live on **1 Apr 2027**; Tranche 2 USD 44,000 (condensate recovery) in 2028

02 **Run the lowest compliant mix:** 45% → 60% → 80% biomass, CO2e ≥ 5% below both caps every year

03 **Gate the 2030 step-up** to 85% / 90% biomass (Option A+) at LSC's 2029 checkpoint: +USD 13.5M revenue

Results

5 / 5 years compliant
CO2e -66.2% by 2031 (target 64%)

USD 134.4M revenue
NPM 8.6% to 9.5%, all floors met

USD 11.6M free cash flow
self-funded, nonewdebt

USD 69.6M revenue at risk
without the roadmap


Why the roadmap must be front-loaded

The 2027 cap, not the budget, sets the timing

LSC LOGISTICS & SUPPLY CHAIN CLUB

01 Growth raises emissions


Heat demand scales with output: **0.0598 GJ per piece** (300,000 GJ ÷ 5.02M pcs). Winning the 2027 orders on coal therefore means:

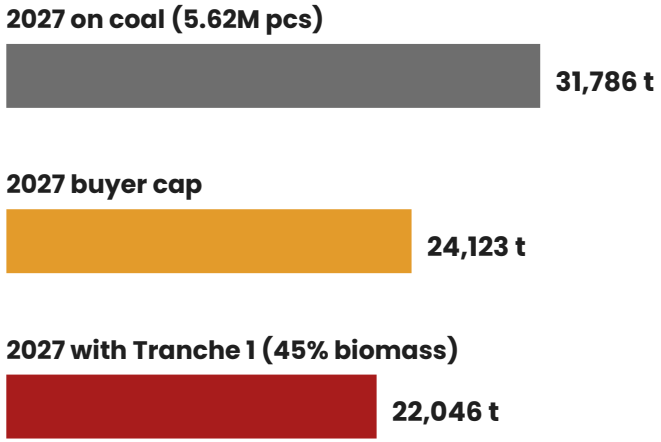

On coal: **31.8% above** the 2027 cap

02 The CAPEX is indivisible

TOTAL PROJECT CAPEX **USD 940,500** (USD 855,000 + 10% contingency) may be phased, not cut.



Firing core = 8 items needed before any biomass can burn:

boiler retrofit, fuel feeding, covered storage, ash handling, filters, fire safety, civil works, engineering and test.

None of them cuts CO2e on its own, so a partial core brings no reduction.

Only condensate recovery (**4.7%**) can move without delaying conversion

03 How hard to run it, 2030–2031

A — Design mix 80% ✓
Output falls to 6.13M pcs

A+ — Biomass 85% / 90% ✓
Holds 8.65M; biomass 1.55× design


A+C — Credits only ✗
Fails 30% off set limit (43% of cap)

A+H — Half biomass, half credits ✓
TOPSIS rank 1: recommended

The real decision is **WHEN** the firing core enters service and **HOW HARD** it runs, not how to spread the cash. Commission Tranche 1 before the 2027 cap applies; defer only condensate recovery to 2028.

CAPEX tranches & commissioning

95.3% of the envelope in service by 1 April 2027

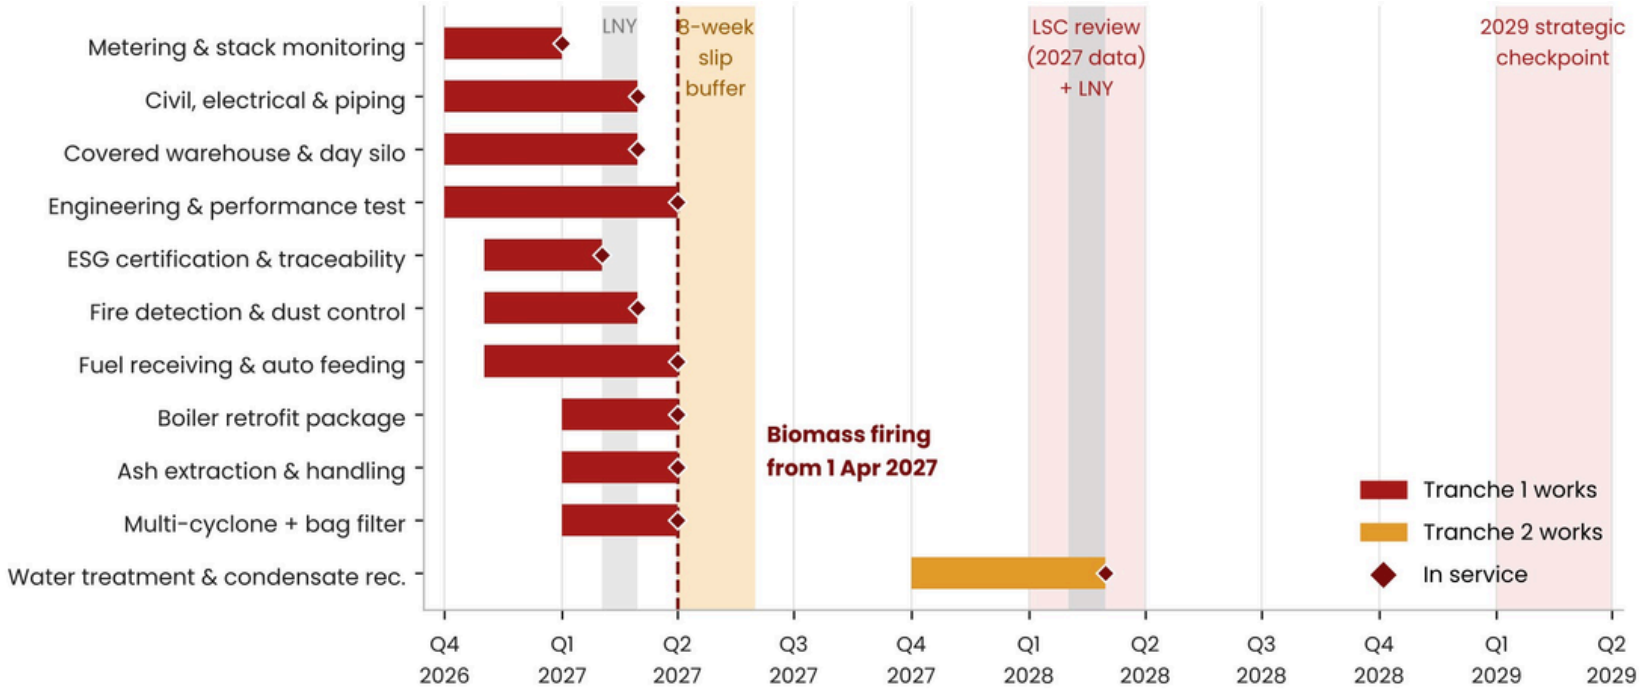

TRANCHE 1 | 2027

USD 896,500 **95.3%**

10 items: firing core (8) + stack/energy metering + ESG traceability

Depreciation USD 179,300 a year, 2027 to 2031

TRANCHE 2 | 2028

USD 44,000 **4.7%**

Water treatment & condensate recovery (efficiency, not compliance)

Depreciation USD 8,800 a year, 2028 to 2032

Jan 2027

Metering live

2027 measured from day one (quick wins + metering)

Feb 2027

Boiler hot works

scheduled into the Lunar New Year shutdown

1 Apr 2027

Biomass firing

performance test closed 31 March

Mar 2028

Tranche 2 live


condensate recovery in the 2028 shutdown

8-week slip buffer (R14)

If commissioning slips to late May, 2027 CO2e = **24,029 t**, still below the **24,123 t** cap.

ESG completion & emission compliance

Within both caps every year; -66.2% by 2031

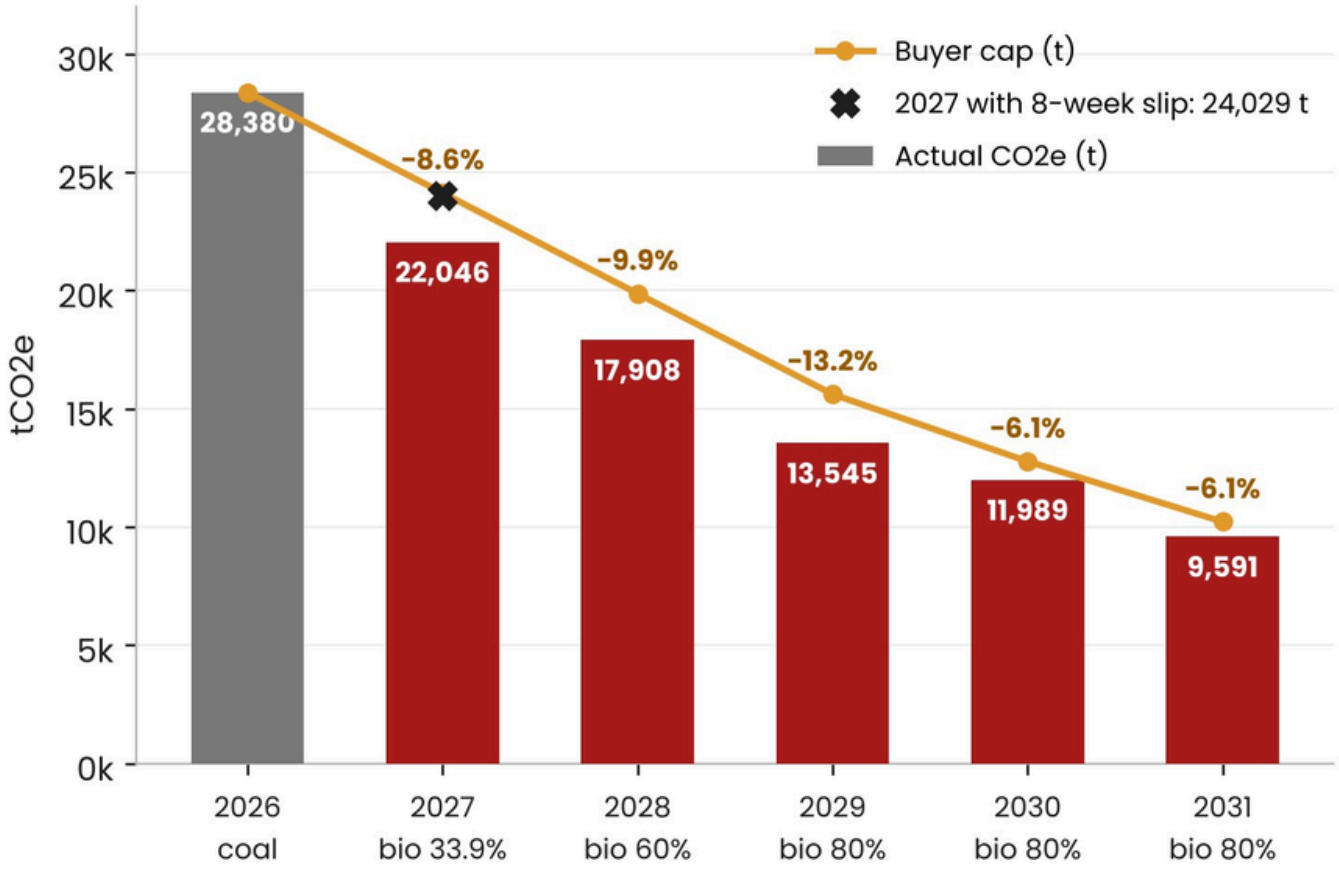


Operating rule

Run the **lowest biomass share in 5% steps** that keeps CO2e **≥ 5% below both** the tonnage and the intensity cap:
45% → 60% → 80% → 80% → 80% (33.9% annual average in 2027, biomass from 1 April)

Cumulative ESG completion

= CAPEX **in service** ÷ USD 940,500. A commitment alone does not count (Emission Target F18).

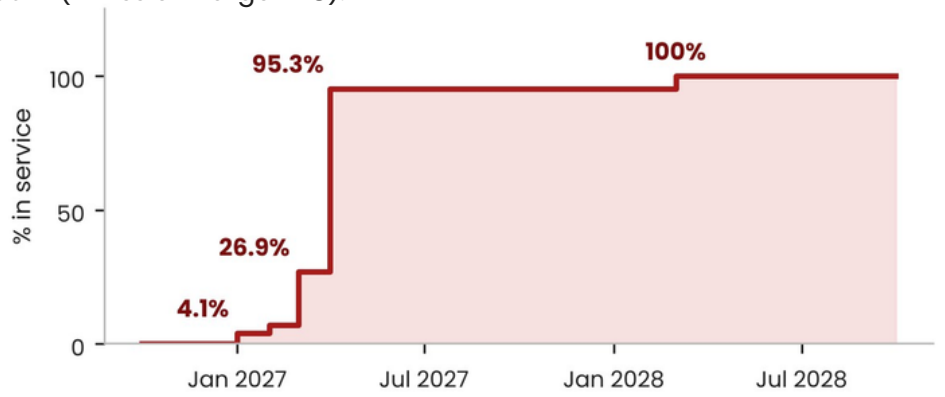


66.2%
CO2e cut by 2031 vs 64% target

5 / 5
years within both caps (6.1%to 13.2%)

95.3%
completion on 1 April 2027

Depreciation: CAPEX to net book value (USD k)

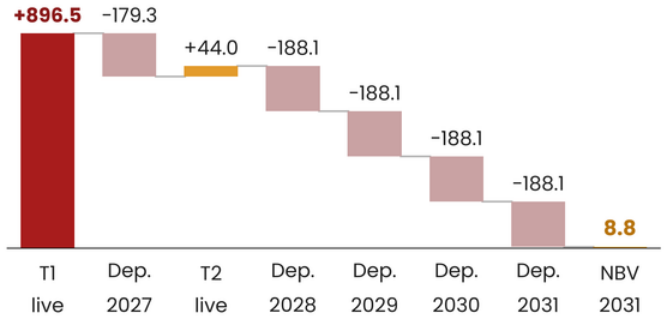

USD 931.7k
expensed 2027 to 2031

USD 8.8k
of Tranche 2 left for 2032

5-year straight line per tranche, no salvage (case rule B27). Replaces CAPEX sheet lives (USD 75,958/yr).

Converting potential orders into sales

The case's own erosion rate sets CR

LSC potential orders

Visibility, not POs (KPI sheet B33)

ESG gate: conversion rate

$CR = (1 + g_{ESG} - |g_{Trad}|) \div (1 + g_{ESG})$

Risk-adjusted demand

Orders × CR

MIN(demand , carbon-allowed capacity)

Capacity = cap ÷ (heat per pc × EF at 78% mix)

Realized sales

5.62M · 6.92M · 8.65M pcs

Why this CR: the Traditional scenario gives the rate at which LSC moves orders away from suppliers whose ESG delivery is **not yet verified** (10%, 12%, 15%). Until each year's review, that share is at risk.

Year	ESG milestone delivered	Challenge	Potential orders	CR	Realized (pcs)
2027	Tranche 1 firing from 1 Apr; 95.3% complete	Moderate	6,124,400	**91.80%**	5,622,400
2028	100% complete; 2027 result verified	Challenging	7,655,500	**90.40%**	6,920,572
2029	Strategic checkpoint passed	High	9,799,040	**88.28%**	8,650,715

CR falls as completion rises

Each milestone is harder (Moderate → Challenging → High) and the case flags "accelerated order loss" in 2029.

Capacity does not bind yet

Caps at the 78% design mix allow 9.10M, 11.91M and 9.36M pcs, all above demand.

Template rates replaced

Pre-filled 90%, 94%, 97% rise over time with no stated basis.

2027 to 2029
potential vs realized


23.58M potential orders › **21.19M** realized pcs › **89.9%** blend conversion

2030–2031 forecast

Carbon, not demand, sets the limit after 2029

Shift-share (Dunn, 1960)


g_{ESG} = market + shift; g_{Trad} = market - shift → market = mean of both (**6.33%** a year)

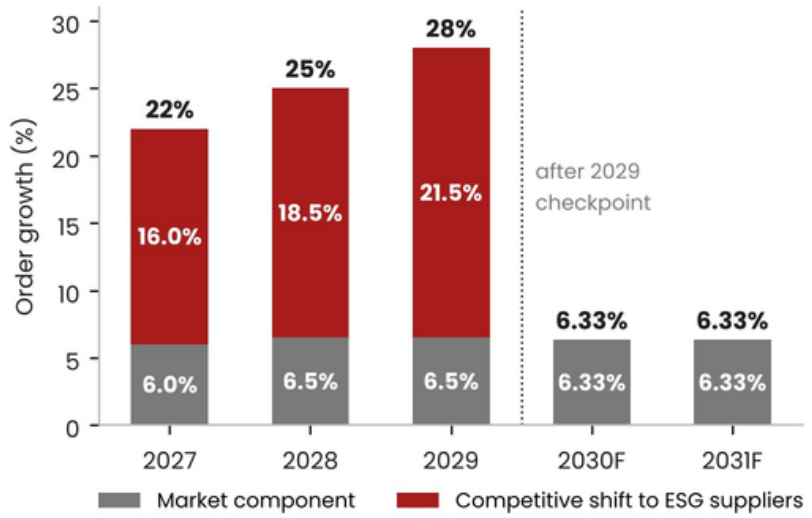

Scenario	Market g	CR	2030	2031
Upside	6.5%	91.8%	9.58M	10.20M
Base	6.33%	88.3%	9.20M	9.78M
Downside	6.0%	86.5%, 84.8%	8.99M	9.33M
Carbon cap (78%)			**7.66M**	**6.13M**

Demand rows=forecast orders × CR (risk-adjusted).

Assumption: upside returns CR to the 2027 level; downside extends the -1.76 pts a year trend.

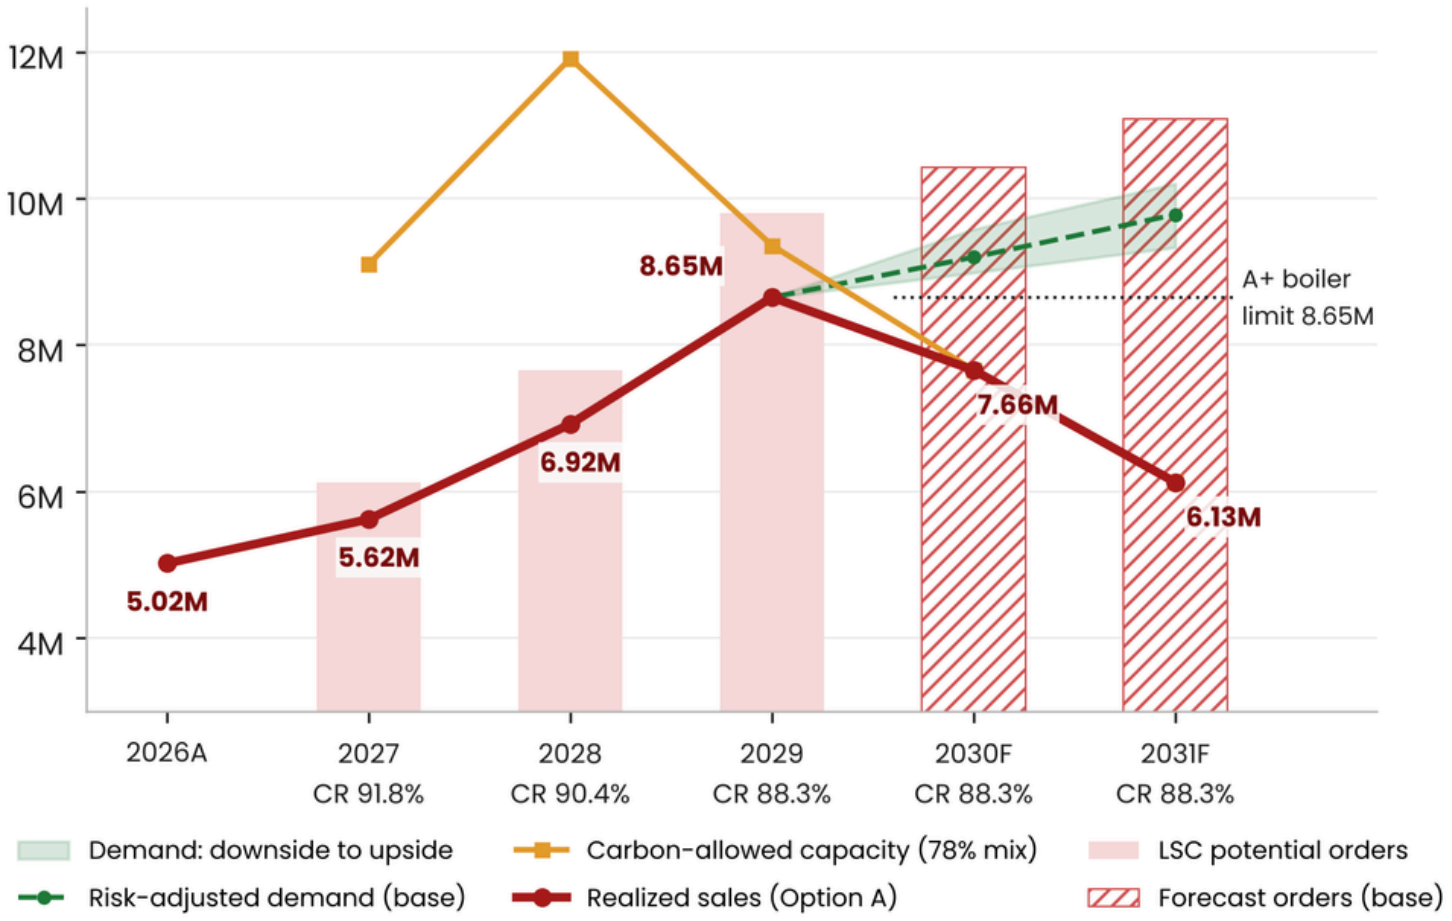


In every scenario demand exceeds carbon-allowed capacity (**≥ 1.33M pcs** in 2030, **≥ 3.21M** in 2031): realized sales are **7.66M and 6.13M pcs** whatever happens to demand. Growth after 2029 is an operating lever.

Five-year P&L

Every annual profit constraint is met with wide headroom

USD thousand	2026A	2027	2028	2029	2030F	2031F
Sales volume ('000 pcs)	5,020	5,622	6,921	8,651	7,657	6,125
Revenue	**19,284**	**21,598**	**26,585**	**33,232**	**29,414**	**23,531**
Base COGS	(15,323)	(17,162)	(21,125)	(26,406)	(23,372)	(18,698)
Gross profit	3,961	4,436	5,460	6,825	6,041	4,833
Incremental ESG OPEX	–	(232)	(488)	(799)	(707)	(569)
Depreciation (ESG CAPEX)	–	(179)	(188)	(188)	(188)	(188)
SG&A	(1,350)	(1,460)	(1,697)	(2,012)	(1,831)	(1,552)
EBIT	2,611	2,565	3,088	3,826	3,3 15	2,525
CIT 20%	(522)	(513)	(618)	(765)	(663)	(505)
Net profit	**2,089**	**2,052**	**2,470**	**3,061**	**2,652**	**2,020**
Net profit margin	**10.83%**	**9.50%**	**9.29%**	**9.21%**	**9.02%**	**8.58%**
Case NPM floor	–	≥ -10%	≥ -8%	> 0%	> 0%	> 0%
Constraint test	–	PASS	PASS	PASS	PASS	PASS

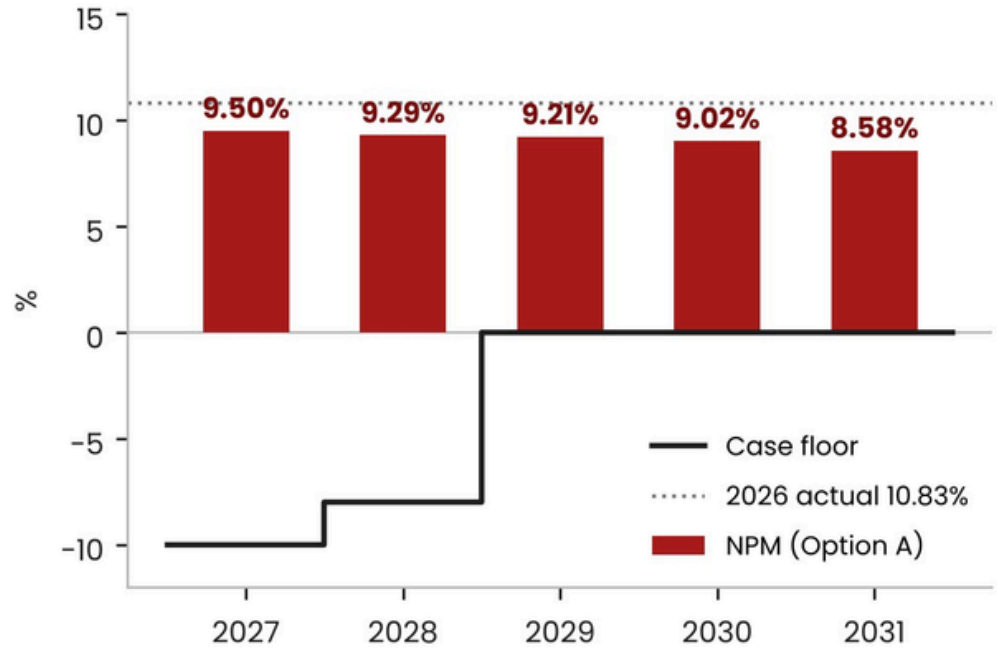

8.58%
lowest NPM (2031)
vs a floor of 0%

-11.3%
EXW price cut needed
to breach any floor


1.9% →3.2%
ESG cost burden
(% of revenue)

Key assumptions

- Revenue= volume× weighted EXW USD 3.8415 (incl. 1.5% to 2.5% ESG premium)
- COGS **USD 3.0525/pc** already carries coal energy → only **incremental** ESG OPEX added
- SG&A **7.0%**: selling 2.5% + G&A 4.5% of 2026 revenue (half fixed); peers MSH 8.5%, TNG 5.4%
  CIT **20%** (Law 67/2025/QH15); FX 25,500; **no new debt**

2027 profit bridge & self-funding

ESG costs: USD 0.41M of USD 4.44M gross profit

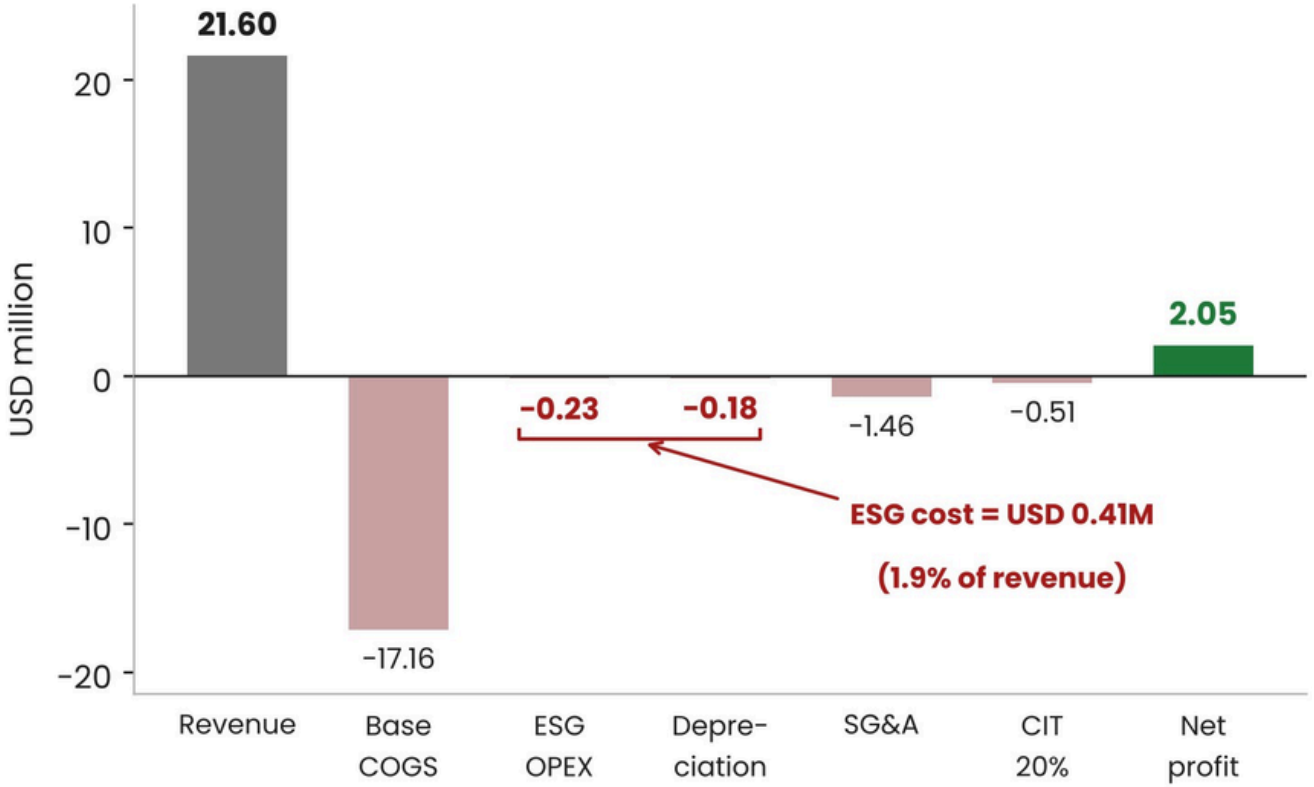

USD million, Option A, 2027 (biomass from 1 April)


CAPEX Coverage Ratio

2027 net profit plus depreciation covers 2.49× the annual CAPEX tranche.

9.50%

2027 NPM vs a floor of -10%: the hardest year is the safest

Free cash flow (USD M)

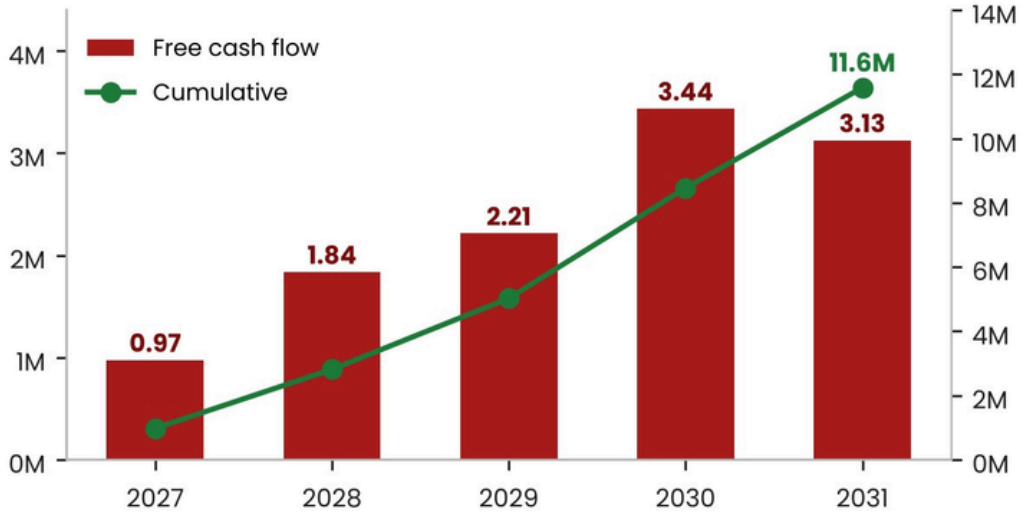

How the roadmap is funded


- Free cash flow is **positive every year** after CAPEX and the working capital growth needs: **USD 11.6M** cumulative by 2031.
- No new debt, so no interest cost; the **2027** tranche is paid from operating cash.
- Working capital: receivables **45**, inventory **45**, payables **30 days** .

Sensitivity & break-even

Commercial terms move profit more than fuel or FX

LSC LOGISTICS & SUPPLY CHAIN CLUB

Tornado: five-year net profit (Option A)

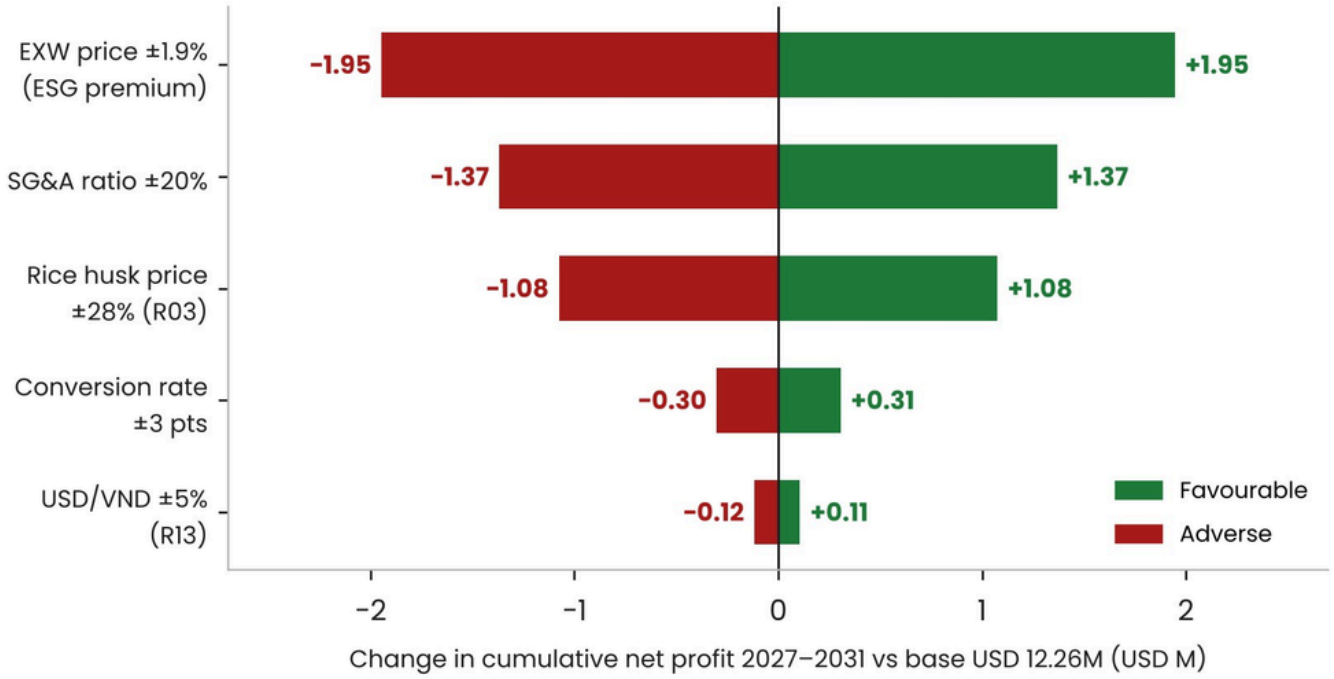

Break-even: change before the first NPM floor fails

Driver	Base	Break-even	Change
EXW price	USD 3.84	USD 3.41	**-11.3%**
Rice husk price	VND 1.95M/t	VND 6.97M/t	**+258% (9× R03)**
SG&A ratio	7.0%	18.4%	**×2.6**
Conversion rate	88% to 92%	13% to 16%	**-75.5 pts**
USD/VND	25,500	≈ 4,700	**not plausible**

ESG premium >> fuel costs

Losing the 1.9% ESG premium costs **USD 1.95M**, almost 2× the R03 rice husk shock (+28%).

CR moves test

±3pts CR moves only USD0.30M: 2030 to 2031

→ volume is capped by carbon, not demand.


Combined stress test (Option A+H)

All six shocks at once: rice husk+28%, boiler efficiency -8%, VND +5%, ESG premium lost, volume -10%, credits at removal price USD 40/t

5.35% **lowest NPM, every floor still met**

ESG pathway vs Traditional

USD 69.6M of revenue at risk without the roadmap

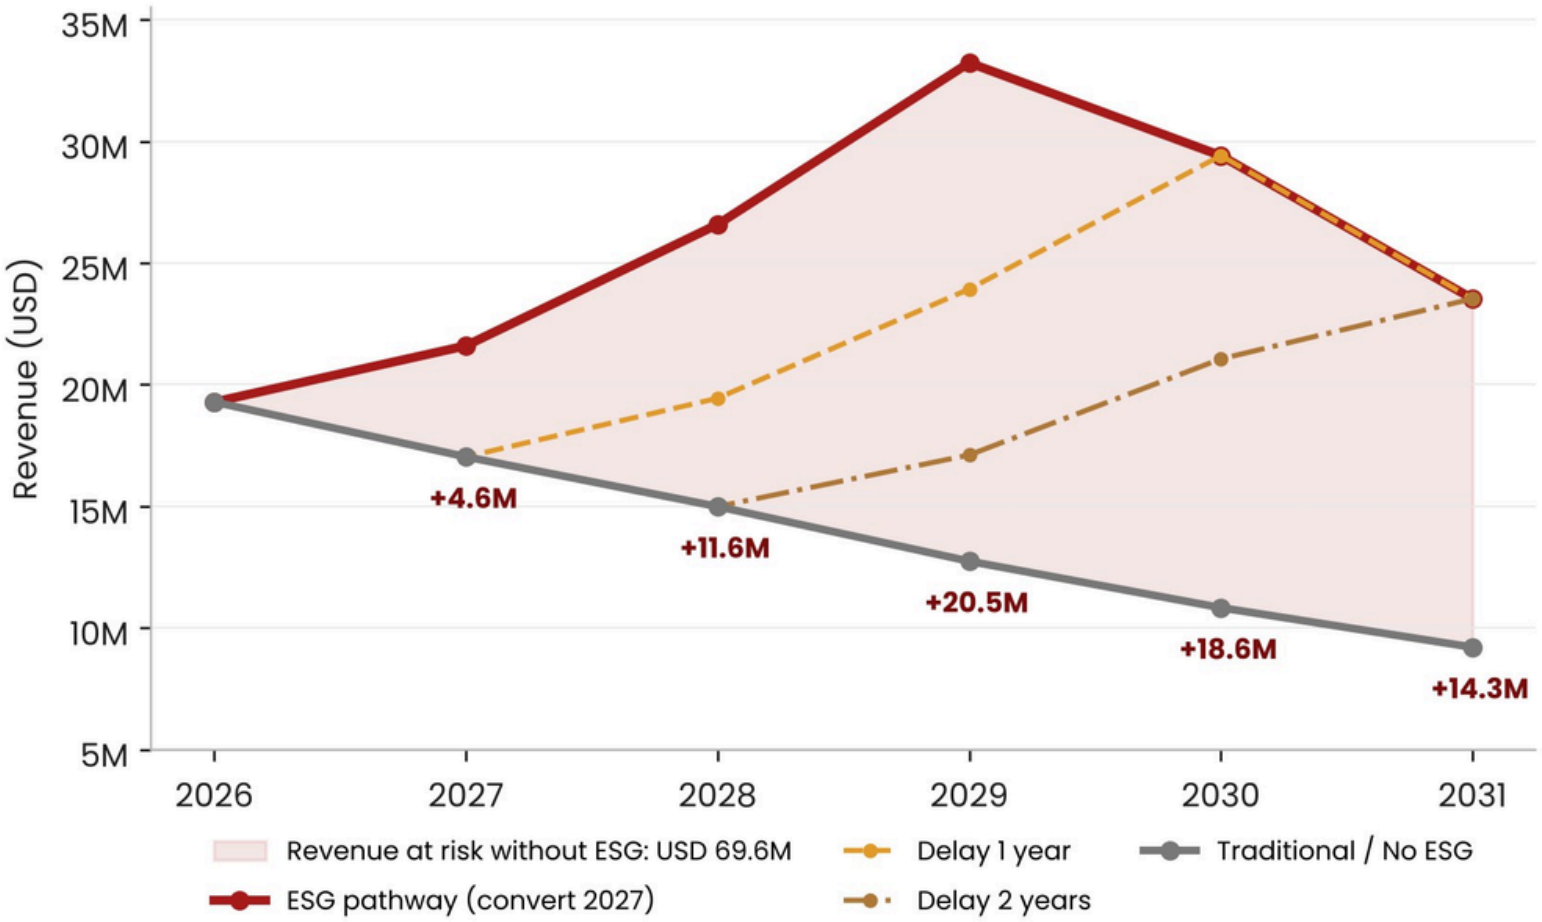

+USD 69.6M

revenue **2027** to **2031**
96% volume, **4%** premium

+USD 6.6M

net profit after all ESG OPEX and depreciation

2030

payback year of incremental free cash flow

94.6 » 80.4


kg CO2e/GJ: Traditional breaches the intensity cap from **2027**

Traditional = coal boiler, base EXW price without premium (USD 3.7698), orders -10%, -12%, -15%, then -15% a year in 2030 to 2031 ("accelerated order loss").

The cost of delay

Each year of waiting costs about USD 20M of revenue

Revenue at risk by year (USD)

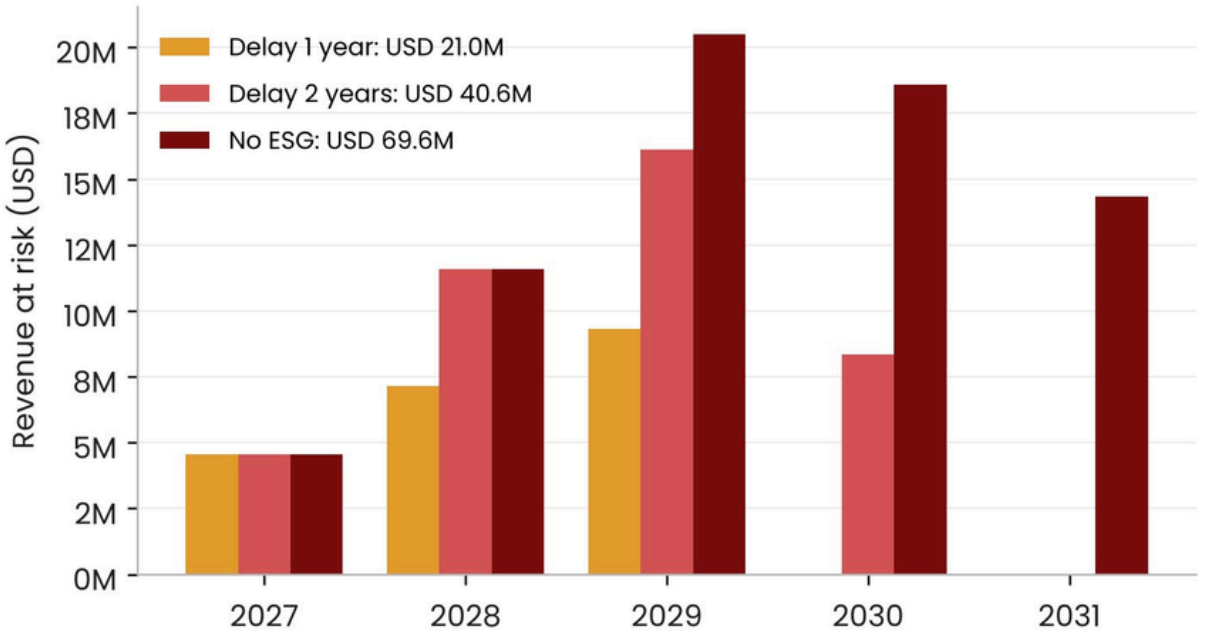

2027 to 2031, USD M	Delay 1 yr	Delay 2 yrs	No ESG
Revenue at risk	**21.0**	**40.6**	**69.6**
Gross profit at risk	4.6	8.8	15.3
Net profit at risk	2.1	4.0	6.6
Years breaching the cap	1 (2027)	2 (2027–28)	5 (all)
Revenue lost per month	1.75	1.69	N/A

≈ USD 1.75M of revenue

is lost for every month the conversion slips past 2027

Orders erode first

On coal, LSC moves 10% to 15% of orders a year to compliant suppliers; the ramp then restarts from a lower base.

Loss sits in 2027 to 2030

By 2031 every converting path reaches the same carbon- allowed capacity, so the loss is never recovered.

Compliance exposure

Each delayed year is a cap breach: LSC may hold, freeze or reallocate allocation (Emission Target H7:H9).

Options, CRITIC weights & TOPSIS

Alternative plans for 2030 to 2031, A+H ranks first

LSC LOGISTICS & SUPPLY CHAIN CLUB

KEY ASSUMPTIONS

① Carbon credits may be bought as "quantified offsets" (Emission Target B20): A to AAA credits at **USD 14.80/t**.

② Credits count toward a buyer cap up to **30% of that cap** (Decree 119/2025 analogy). From 2030 the cap binds, so below are the alternative plans.

A — Design mix (Base case)
80% biomass, no credits
Output falls to 6.13M pcs in 2031

A+ — Biomass step-up (Alternative 1)
85% / 90% biomass
Holds 8.65M pcs; peak biomass 1.55× design

A+C — Credits only (Alternative 2)
80% biomass + 6,630 t credits
Holds 8.65M pcs; credits up to 43% of 2031 cap

A+H — Half and half (Selected plan)
82.5% / 85% + 3,315 t credits
Holds 8.65M pcs; credits ≤ 21.6% of a cap

Criterion group	Criterion	B/C	w	A	A+	A+C	A+H
Growth	C1 Cumulative revenue (USD M)	B	**11.1%**	134.36	147.88	147.88	**147.88**
	C2 Sales 2031 ÷ 2026 (×)	B	**11.1%**	1.22	1.72	1.72	**1.72**
Profit-ability	C3 Cumulative net profit (USD M)	B	**10.9%**	12.26	13.59	13.63	**13.61**
	C4 Lowest NPM	B	**10.5%**	8.58%	8.99%	9.05%	**9.02%**
Cash flow	C5 Cumulative FCF (USD M)	B	**15.0%**	11.58	11.41	11.44	**11.43**
	C6 Lowest annual FCF (USD M)	B	**0.0%**	0.97	0.97	0.97	**0.97**
ESG	C7 Credit cost (USD k)	C	**13.6%**	0	0	98.1	**49.1**
	C8 CO2e cut 2031, in-boundary	B	**12.6%**	66.2%	67.8%	52.3%	**60.1%**
Execution risk	C9 Peak biomass ÷ design (×)	C	**15.2%**	1.38	1.55	1.38	**1.46**

Pink = best value per criterion; grey = worst. B = benefit, C = cost; w = CRITIC weight (contrast × conflict).

Interpretation & conclusion

- **A+, A+C and A+H** all hold 8.65M pcs, so growth ties; the plans differ on **cash, credit cost, in-boundary CO2e and biomass tonnage**, which CRITIC weights most.
- **A+H** is the balanced plan: half the extra tonnage of A+, half the credit bill of A+C, profit and FCF above A+.
- **Conclusion:** adopt **A+H**; switch to A+ at the 2029 checkpoint if LSC refuses offsets or credits exceed USD 21.2/t.

Ranking result	A	A+	A+C	A+H
TOPSIS CC (main)	**0.5597 (3)**	**0.5661 (2)**	**0.5468 (4)**	**0.5750 (1)**
VIKOR Q (lower = better)	0.500 (2)	0.500 (2)	0.549 (4)	**0.427 (1)**
SAW score	0.551 (4)	0.680 (1)	0.617 (3)	**0.648 (2)**
Offset gate (≤ 30% of cap)	Pass	Pass	Fail (43%)	**Pass**
Selected (rank 1, TOPSIS + VIKOR)				**A+H**

Recommendation

Front-load now; cover 2030 to 2031 with half biomass, half credits

Q4 2026	1 Apr 2027	Mar 2028	2029	2030 to 2031
Commit Retrofit+ 3 index-linked fuel contracts; metering live 1 Jan	**Tranche 1 live** USD 896,500; biomass 45%	**Tranche 2 live** USD 44,000; biomass 60%	**GATE** Checkpoint: agree offsets with LSC; 80% biomass at peak	**A+H** 82.5%/ 85% biomass + 3,315 t A to AAA credits

2029 switch rule: run A+H only if ALL hold

- **LSC accepts offsets** — quantified offsets (Emission Target B20); else step up to A+
- **Credit price ≤ USD 21.2/t** — break-even vs the biomass step-up
- **Credits rated A to AAA** — or ICVCM CCP label; reported apart (R06, R07)
- **Credits ≤ 30% of a cap** — A+H needs at most 21.6% (offset limit)
- **Supply gates for any step-up** — OTIF ≥ 95%, 3 suppliers, moisture ≤ 12%, efficiency ≥ 92%

What A+H buys (vs Option A)

2027 to 2031	A	A+H	Change
Revenue (USD M)	134.4	147.9	+13.5
Net profit (USD M)	12.26	13.61	+1.36
2031 output (M pcs)	6.13	8.65	+41%
CO2e cut 2031, net of credits	6.2%	67.8%	+1.6 pts
Lowest NPM, all 6 shocks	–	5.35%	PASS



Anchor the 1.9% ESG premium in the supply agreement against the annual KPI pack




Index-link biomass prices so fuel inflation is shared, not absorbed



Fund from operating cash: no new debt, FCF positive every year

Risk management: Top 5

Ranked by score and by what TEXIN controls

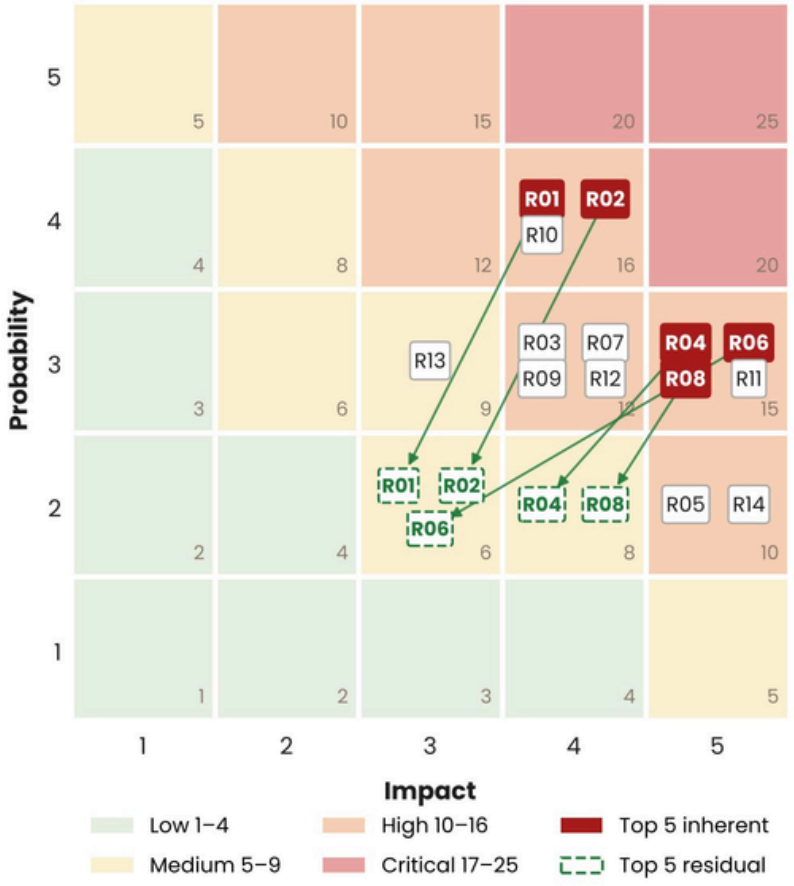

Risk (P × I)	Trigger / KPI	Prevent + respond	Residual	Owner
R01 Rice husk supply in rainy season (16)	Supplier OTIF < 85%	3 approved suppliers; 10 to 14 day covered buffer before the rains; switch share to wood pellet	**2×3 = 6**	Procurement
R02 Moisture → 18% 10% (16)	Moisture > 12% at receiving	Spec ≤ 10%; test every lot with rejection rule; covered FIFO storage; blend wood pellet	**2×3 = 6**	QA + Utilities
R04 Silica ash fouling (15)	Efficiency -8%; cleaning doubles	Redesigned PM and cleaning cycle; critical spares; higher wood pellet share	**2×4 = 8**	Engineering
R06 Incomplete fuel traceability (15)	Lot without chain- of-custody	Lot-level chain-of-custody; annual supplier audit; unproven lots excluded from CO2e claims	**2×3 = 6**	ESG + Procurement
R08 Steam pressure hits dyeing (15)	Temperature deviation > spec	Steam KPI linked to dyeing QC; load test at 1.72× before the 2029 peak	**2×4 = 8**	Production

Residual scores are the team's assessment after mitigation; inherent scores from the case risk register.

Watch list: R09, R10, R11 (12 to 16) act on TEXIN only indirectly: under EXW the buyer controls main transport (EXW Price D18).
R03, R13, R14 are quantified in the stress tests.

Implementation roadmap & KPI dashboard

Each KPI has a target and a trigger

LSC LOGISTICS & SUPPLY CHAIN CLUB

	SHORT TERM: BUILD & CONVERT		LONG TERM: OPERATE, VERIFY & SCALE		
	Q4 2026	Q1 2027	Apr 2027 to 2028	2029	2030 to 2031
Actions	Sign retrofit and 3 index-linked fuel contracts; civil works; metering live 1 Jan	Boiler works in LNY shutdown; build 10 to 14 day covered buffer; performance test	Biomass 45% then 60%; Tranche 2 in 2028 shutdown; first LSC verification	80% biomass at 1.72× peak load; checkpoint: agree offsets with LSC	A+H: 82.5% / 85% biomass + 3,315 t A to AAA credits
KPI target	Contracts signed; metering live on 1 Jan 2027	Performance test passed by 31 Mar 2027	CO2e run-rate ≥ 5% below pro-rata cap; OTIF ≥ 95%; moisture ≤ 10%	Boiler efficiency ≥ 92%; steam in spec; NPM headroom ≥ 5 pts	2031 cut ≥ 64% net; credits ≤ 30% of cap; full chain-of-custody
Trigger → response	Contract late > 4 weeks → escalate to the board	Slip > 4 weeks → fast-track spares and crew	Run-rate > 95% of cap → +5% biomass step	Offsets OK, ≤ USD 21.2/t → A+H; else A+ or A	Credits > USD 21.2/t or refused → step up to A+
Outcomes	**4.1%** ESG completion (metering live)	**95.3%** completion; CO2e -8.6% under cap	**100%** completion; NPM 9.3% (2028)	**USD 33.2M** peak revenue; 8.65M pcs held	**-67.8%** net CO2e vs 2026; USD 11.4M FCF

Appendix A: Key assumptions

How missing or conflicting case data were handled

Issue in the case data	Resolution adopted	Basis
Heat demand fixed at 300,000 GJ while volume almost doubles	Heat scales with output: 0.0598 GJ per piece	ESG_CAPEX OPEX B6, D6 (dyeing/finishing steam)
"78% biomass gives 64%" but workbook factors give 70.5%	Workbook emission factors; 78% kept as design mix for capacity	CO2 Emission Calculation; Emission Target F11
CAPEX sheet depreciates by component life	5-year straight line per tranche (case rule)	Sales Forecast & Case 2A KPI B27
COGS already contains coal-based energy	Only incremental ESG OPEX above coal is added	COGS sheet; ESG_CAPEX OPEX F45 (VND 14.83 bn reconciled)
EXW price already includes the ESG premium	Traditional priced at base EXW without premium	EXW Price E6:F10
No SG&A, interest or tax given	SG&A 7.0% (half of G&A fixed); CIT 20%; no new debt	MSH H1 2024 (FireAnt); TNG Q4 2025 (BSC); Law 67/2025/QH15
Template conversion rates 90%, 94%, 97%	Rates derived from the case erosion rates	Sales Forecast D10:D12; Emission Target B18:B19
2030 to 2031 constraint worded differently	Stricter version: net profit > 0 and NPM > 0%	Case brief Table 3; KPI sheet B32
No boiler rating given	Retrofit supplies up to 1.72× 2026 heat; A+ volume capped there	ESG_CAPEX OPEX J17; flagged as R08
No working capital terms	Receivables 45, inventory 45, payables 30 days	Team assumption, used for free cash flow only
No carbon credit price or offset rule	USD 14.80/t (A to AAA credits); credits count up to 30% of a cap	Regreener (MSCI, Allied Offsets); Decree 119/2025 via VnEconomy

Appendix B: CAPEX detail

11 items, 2 tranches, incl. 10% contingency (USD)

CAPEX item	Priority	Tranche 1 (2027)	Tranche 2 (2028)	Works start	In service
Biomass boiler/furnace retrofit	Critical	308,000		Jan 2027	Apr 2027
Fuel receiving, conveyor & feeding Covered warehouse & day silo	Critical	132,000		Nov 2026	Apr 2027
Multi-cyclone + bag filter	Critical	93,500		Oct 2026	Mar 2027
Fire detection & dust control	Critical	104,500		Jan 2027	Apr 2027
Ash extraction & handling	Critical	33,000		Nov 2026	Mar 2027
Civil, electrical & piping	High	49,500		Jan 2027	Apr 2027
Engineering, commissioning & test	High	60,500		Oct 2026	Mar 2027
Stack emission & energy metering	High	49,500		Oct 2026	Apr 2027
ESG certification & traceability	High	38,500		Oct 2026	Jan 2027
Water treatment & condensate recovery **Total per tranche**	Medium	27,500		Nov 2026	Feb 2027
Share of envelope (USD 940,500)	Medium		44,000	Oct 2027	Mar 2028
Annual depreciation (5-year straight line)		**896,500**	**44,000**		
		95.3%	4.7%		
		179,300	8,800		

Appendix C: References

Sources used in the report and the workbook: **WORKBOOK.xlss**

1. BSCResearch. (2026,January 21).X-Stock | TNG:Secured orderbook. https://www.bsc.com.vn/en/bao-cao/15523-x-stock-tng-vnd25500-21-secured-orderbook
2. Diakoulaki, D., Mavrotas, G., & Papayannakis, L. (1995). Determining objective weights in multiple criteria problems: The CRITIC method. Computers & Operations Research, 22(7), 763–770.
3. Dunn, E. S. (1960). A statistical and analytical technique for regional analysis. Papers of the Regional Science Association, 6(1), 97–112.
4. FireAnt. (2024, June 28). CTCP May Sông Hồng (MSH): Business results H1 2024. https://static.fireant.vn/Upload/AttachedFiles/MSH.pdf
5. Hwang, C. L., & Yoon, K. (1981). Multiple attribute decision making: Methods and applications. Springer.
6. LogiChain 2026 Organizing Committee. (2026). Data Case Study 2A: TEXIN [Case brief and Excel workbook]. NEU Logistics & Supply Chain Club.
7. National Assembly of Vietnam. (2025). Law on Corporate Income Tax No. 67/2025/QH15, Article 10(1).
8. Regreener. (n.d.). Voluntary carbon market update: Prices and trends. https://www.regreener.earth/blog/voluntary-carbon-market-update
9. VnEconomy. (2026, February 15). Legal framework for carbon market to be finalized. https://en.vneconomy.vn/legal-framework-for-carbon-market-to-be-finalized.htm
10. Team workbook: PHỤ LỤC | Supernova.xlsx, submitted as PHỤ LỤC (all formulas live).
